
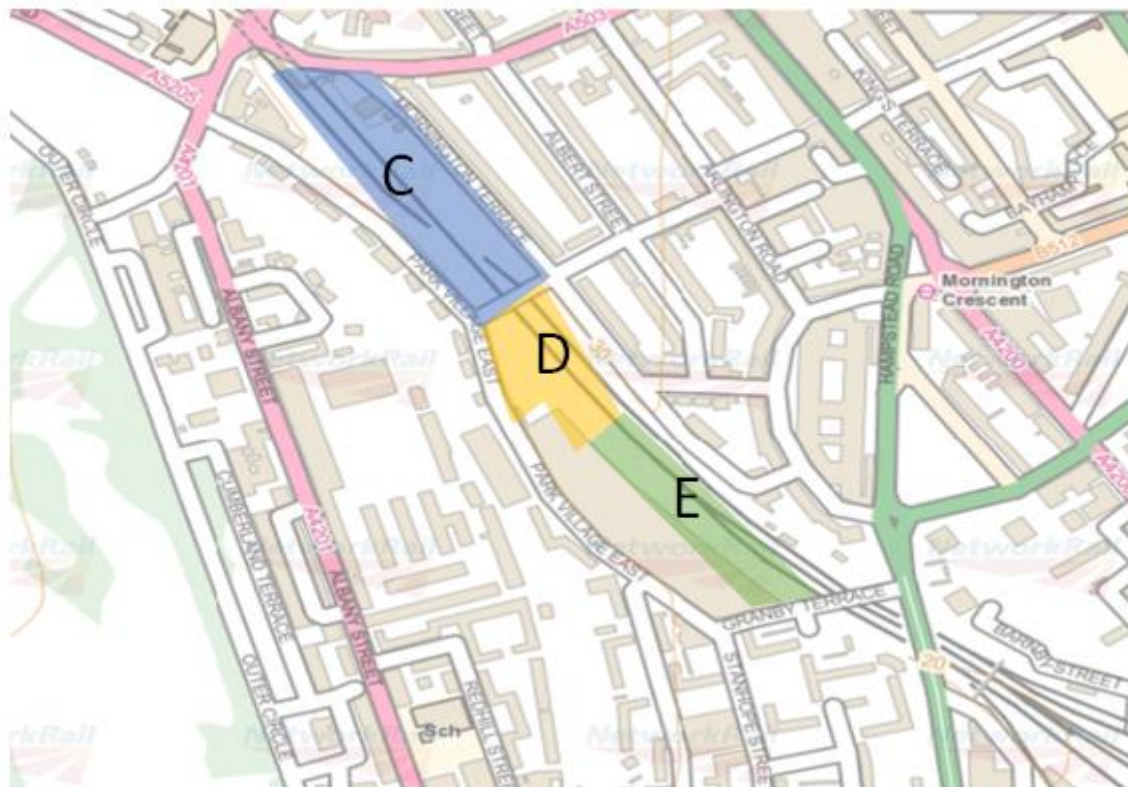


Appendix A: Maps of work locations

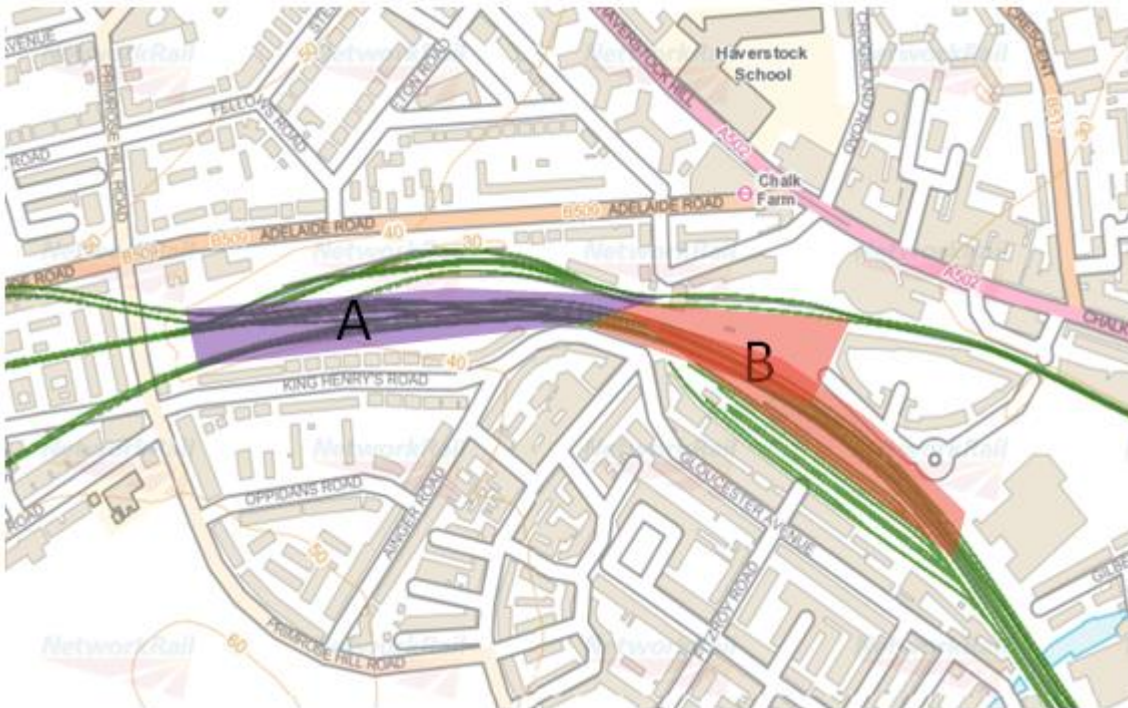

Appendix B: Details of works

Dates	Working hours	Zone(s) (as marked on Appendix A)	HS2 related works
1-2 April 2017	21.00 - 11:15	D, E	Overhead line and permanent way activities. Snagging works and contingency to remove any remaining scrap.
5-7 April 2017	23.30 - 05:25	D, E	Installation of steel plates and contingency for installing timbers.
8-9 April 2017	21:00 - 11:15	B,D,E	Overhead line and permanent way activities. Snagging works and contingency to remove any remaining scrap. Contingency for snagging 00:40 – 06:45 09 April 2017 in Area B. Transport and install steel plates. Spoil clearance.
10-14 April 2017	08:00 – 18:00	D,E	Concrete pour to ramp, install safety barrier
15-17 April 2017	20:00 - 06:45	D,E	Overhead line activities. Steel plate installation. Contingency for completion of minor.
17-21 April 2017	08:00 – 18:00	D,E	Installation of steel plates and contingency for completion of other works.
22-23 April 2017	20:00- 12:00	D,E	Removing scrap and contingency for completion of other works and snagging.
24-28 April 2017	08:00 – 18:00	D,E	Removing scrap and contingency for completion of other works and snagging.
28 April – 1 May 2017	20:00 - 06:45	A,B,C,D,E	Snagging works and general site works.
1-5 May 2017	08:00 – 18:00 & 23:00 – 05:30	A,B	Concrete works to break out and replace a haunch, re-grit steel plates and snagging works
5-8 May 2017	20:00 - 06:45	C,D,E	Snagging works
9 May – July 2017	To Be Confirmed	To Be Confirmed	Information relating to these works will be provided at a later date once the works programme is confirmed
