
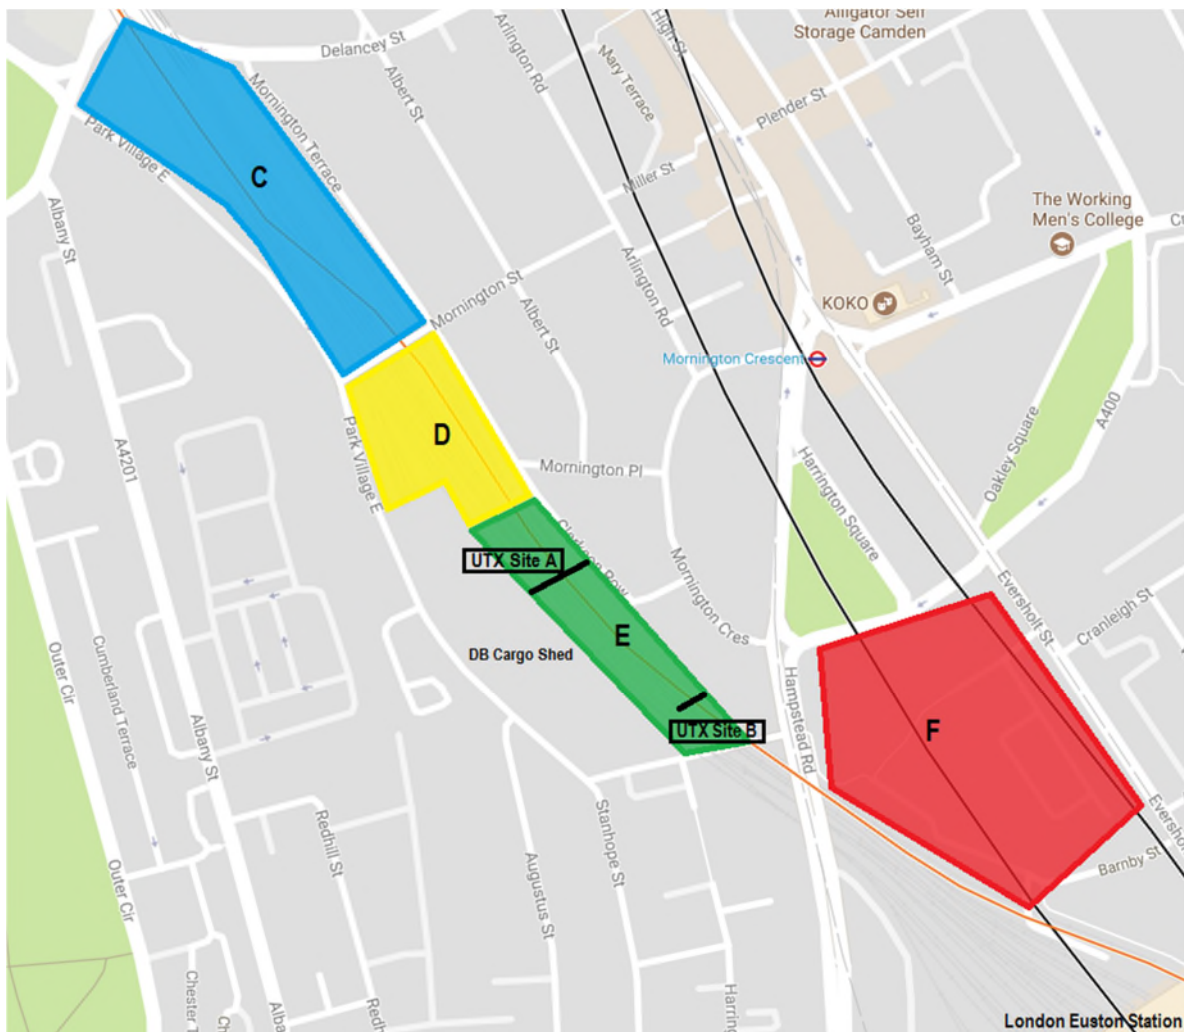


Appendix A: Maps of work locations

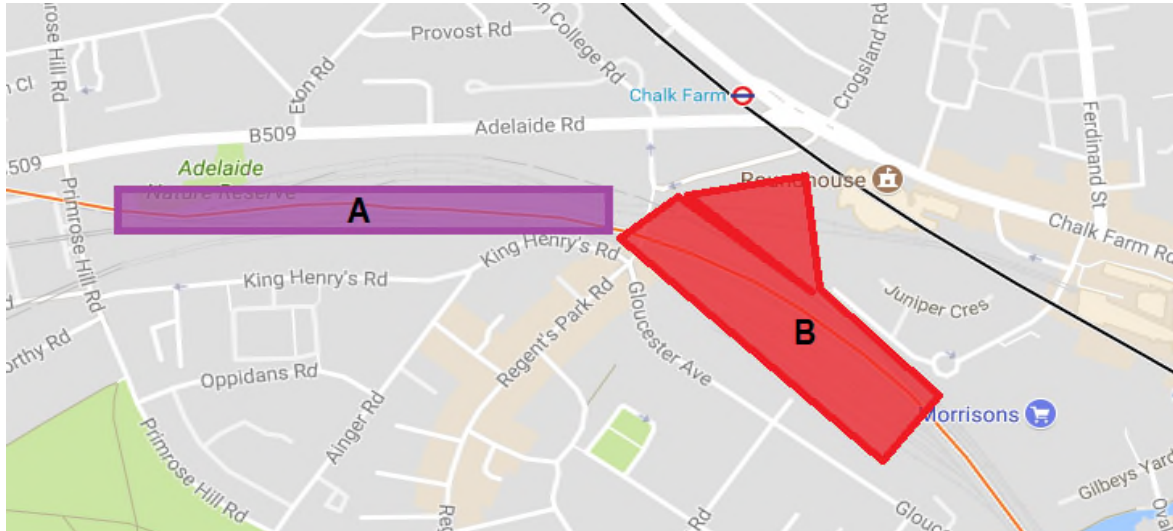

Appendix B – Details of Works

Euston throat Network Rail HS2-enabling works (subject to addition & change at short notice)

Dates	Working Hours	Zone(s) (as marked on Appendix A)	HS2 related works
29 January – 9 February 2018	08:00 – 18:00	B,C,D & E	Deliveries by lorry to new offices at Juniper Crescent Cable percussive borehole drilling during day time hours.
2 February – 9 February 2018	08:00 Sat – 18:00 Sat 20:00 Sat - 12:00 Sun 23:30 Sun - 05:30 Mon 08:00 – 17:00 Mon - Fri	B,C,D & E	Spoil and scrap removal. Track monitoring at new crossing. Ballast compaction as required. Delivery of drilling rig during night shifts, Area B. Drilling during day shifts. Trial holes, civils structures works, building, signage and cabinet footings. Possible construction work to complete the two Under Track Crossings (UTX's)
10 February – 18 February 2018	08:00 Sat – 18:00 Sat 20:00 Sat - 12:00 Sun 23:30 Sun - 05:30 Mon 08:00 -17:00 Mon - Fri	B,C,D & E	Spoil and scrap removal. Track monitoring at new crossing. Ballast compaction as required. Delivery of drilling rig during night shifts. Drilling during day shifts. Re-siting of drilling rig. Possible construction work to complete the two Under Track Crossings (UTX's)
10 February – 11 February 2018	20:00 – 12:00	E & F	Installation of crane on Granby Terrace Bridge. Removal of transformer and materials from DB Shed exterior by crane onto transporter wagons. Contingency following weekend.
17 February – 18 February 2018	20:00 – 12:00	E & F	Contingency for Installation of crane on Granby Terrace Bridge. Removal of transformer and materials from DB Shed exterior by crane onto transporter wagons.

Dates	Working Hours	Zone(s) (as marked on Appendix A)	HS2 related works
17 February – 23 February 2018	08:00 Sat – 18:00 Sat 20:00 Sat - 12:00 Sun 23:30 Sun - 05:30 Mon 08:00 – 17:00 Mon - Fri	B,C,D, E & F	Spoil and scrap removal. Track monitoring at new crossing. Ballast compaction as required. Delivery of drilling rig during night shifts. Drilling during day shifts. Ground Investigation with probe using track vehicle Possible construction work to complete the two Under Track Crossings (UTX's)
24 February – 02 March 2018	08:00 – 18:00 Mon - Fri 21:00 – 07:00 Mon - Fri	B,C,D & F	Equipment deliveries. Ground investigations. Rotary drilling Non-intrusive trial holes in Zone F
3 March - 5 March 2018	20:00 Sat - 05:00 Mon	A,B,C,D & E	Material deliveries for signalling equipment. Construction of signalling bases. Removal of lighting Towers. Removal of drilling rig (05 Mar) Area B. Possible construction work to complete the two Under Track Crossings (UTX's)
10 March - 11 March 2018	20:00 Sat – 11:15 Sun Sun 00:40 – 0645 Sun	A,B,C,D & E	Material deliveries for signalling equipment. Construction of signalling bases. Removal of lighting towers
17 March – 18 March 2018	20:00 Sat – 11:15 Sun Sun 00:40 – 0645 Sun	A,B,C,D & E	Material deliveries for signalling equipment. Construction of signalling bases. Removal of lighting towers
25 March – 26 March 2018	20:00 Sat – 11:15 Sun Sun 00:40 – 0645 Sun	A,B,C,D & E	Material deliveries for signalling equipment. Construction of signalling bases. Removal of lighting towers
27 March – 31 March 2018	08:00 Sat – 18:00 Sat 20:00 Sat - 12:00 Sun 23:30 Sun - 05:30 Mon 08:00 – 17:00 Mon - Fri	A,B,C,D & E	Material deliveries. General track & points maintenance and monitoring (NR) as required. Deliveries to access point and offices at Juniper Crescent Ground investigation work. Possible ballast compaction activities (NR)

Barnby Street Electrical Substation Works

Dates	Working Hours	Zone(s) (as marked on Appendix A)	HS2 related works
<p>31 January to December 2018</p> <p>(Main building work scheduled for completion August 2018 then fit out and bringing into use post-Christmas 2018)</p>	<p>08:00 – 18:00</p>	<p>F</p>	<p>Replacement of Electrical sub-station at Barnby Street continues.</p> <p>January 2018 secondary excavation down to final level followed by reinforced concrete raft construction.</p> <p>Installation of new drainage system. Stop/Go boards in use for entry & exit to Ampthill Estate for 1 day in February.</p> <p>Carpentry work, pouring concrete foundations, constructing brick and block work.</p>
