
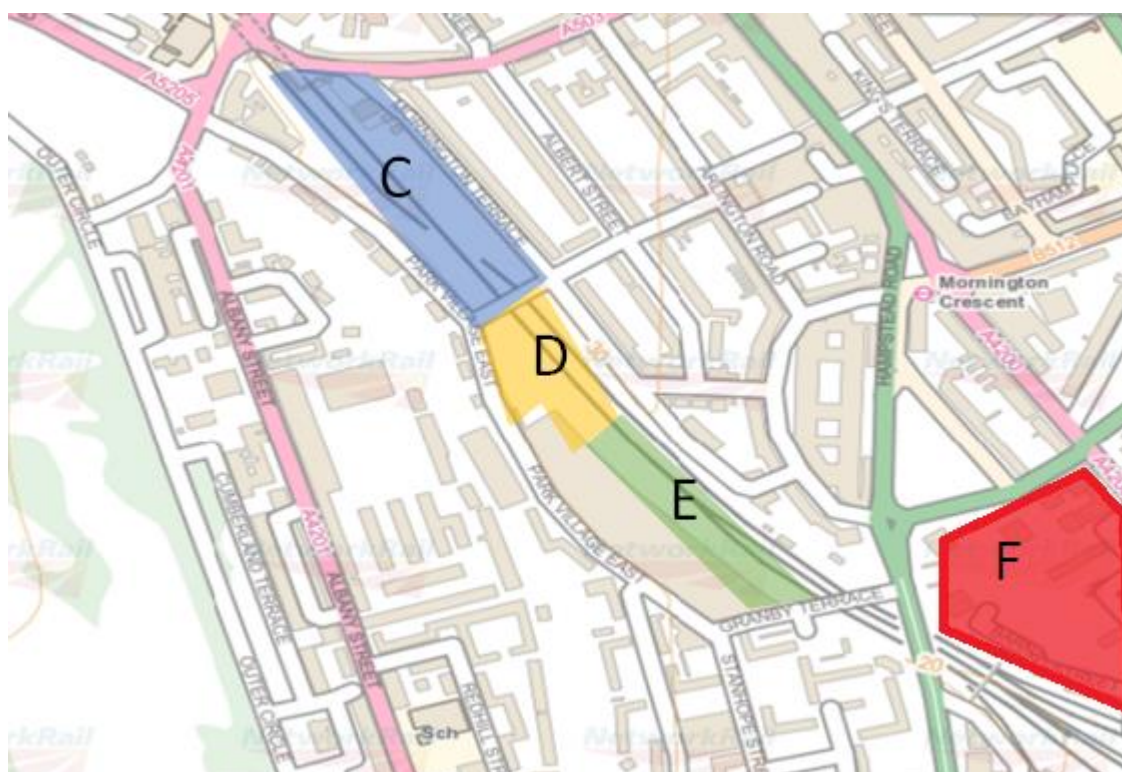


Appendix A: Maps of work locations

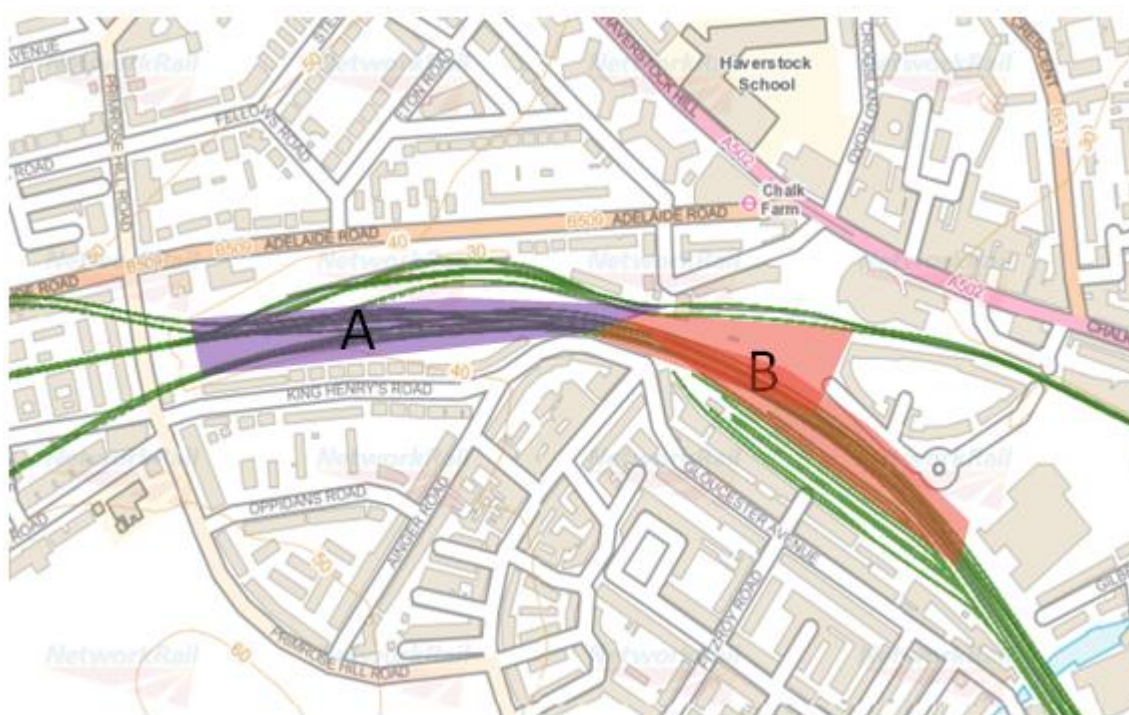

Appendix B – Details of Works

Euston Throat Network Rail HS2-enabling works

Dates	Working Hours	Zone(s) (as marked on Appendix A)	HS2 related works
28-29 October	20:00 – 12:00	B,C,D & E	Delivery of materials and equipment. Spoil removal, cable installation and diversions and excavation for drainage trough. Install driver's walkway.
30 October - 3 November	08:00 – 18:00	B,C,D & E	Delivery of materials and equipment. Track removal and drainage trough excavation. Cable diversions and wall removal. Minor asbestos removal.
30 October – 1 November	21:00 – 11:15	B,C,D & E	Non-intrusive surveys. Hand tools only
1 – 2 November	22:00 – 06:00	E	Delivery of equipment and materials.
4 - 5 November	20:00 – 12:00	B,C,D & E	Install driver's walkway. Clear spoil from site and egress machines via Juniper Crescent.
4- 5 November	20:00 – 12:00	C, D & E	Trial pits. Hand tools only.
5 November	08:00 – 18:00	B	Track bed investigation Camden carriage sidings.
4 - 6 November	20:00 – 05:30	B,C,D & E	Delivery of equipment and materials. Install new driver's walkway. Installation of new lighting columns. Ground investigations, trial holes using hand tools.
6 – 10 November	07:00 – 17:00	E	Internal wood and non-structural fittings manually removed from lineside structures ahead of mechanical demolition.
4 November – 22 December	08:00 – 17:00	E	Removal of waste materials. Environmental checks.
11 – 12 November 18 – 19 November 26 – 27 November	21:00 – 12:00	B,C,D & E	Delivery of equipment and materials. Installation of concrete bases. Installation of equipment. Demolition of lineside structures Site E & material removal.
12 November	08:00 – 18:00	B	Trial pits. Hand tools only. Coring inside redundant building Camden carriage sidings.
Dates	Working Hours	Zone(s) (as marked on Appendix A)	HS2 related works

19 November	08:00 – 18:00	B	Trial pits. Hand tools only. Coring inside redundant building Camden carriage sidings.
25 -26 November	22:00 – 06:00	A, D & E	Delivery of equipment and materials. Building demolition. Material removal. Ground investigations. Trial pits. Hand tools only. High Level surveys using mobile elevated working platform.
26 November	08:00 – 18:00	B	Surveys of Camden carriage sidings.
27 November – 1 December	08:00 – 17:00	D	Trial pits. Hand tools only.
27 November – 22 December	22:00 – 06:00	F to Euston Station	Ground Investigations.
2 - 3 December	20:00 – 12:00	A,C,D & E	Ground investigations. Trial pits. Hand tools only. High level surveys using mobile elevated working platform. Delivery of equipment and materials. Installation of driver's walkway & lighting bollards.
3 December	08:00 – 18:00	B	Surveys of Camden carriage sidings.
4 to 22 December	08:00 – 17:00 Mon -Fri	B,C,D & E	Non-intrusive surveys, Trial holes etc. hand tools only. Material deliveries. Material removal.
3 December	08:00 – 18:00	B	Surveys of Camden carriage sidings.
5 – 6 December	22:00 – 06:00	F to Euston Station	Trial pits. Hand tools only.
Dates	Working Hours	Zone(s) (as marked on Appendix A)	HS2 related works
7 December	22:00 – 06:00	E	Delivery of equipment and materials.
9 - 10 December	20:00 – 12:00	A,C,D & E	Ground investigations. Delivery of equipment and materials.

			Installation of driver's walkway & lighting bollards.
10 December	08:00 – 18:00	B	Ground investigations of Camden carriage sidings.
11 – 14 December	22:00 – 06:00	F to Euston Station	Ground investigations.
16 – 17 December	20:00 – 12:00	B,C,D & E	Ground investigations. Delivery of equipment and materials. Installation of driver's walkway & lighting bollards.
17 December	08:00 – 18:00	B	Ground investigations of Camden carriage sidings.
27 – 28 January 2018	20:00 – 12:00	B,C,D & E	Delivery of equipment and materials. Install new cables.

Barnby Street electrical substation works

Dates	Working Hours	Zone(s) (as marked on Appendix A)	HS2 related works
30 October – 3 November	08:00 – 18:00	F	Installation of piling platform
6 November – 22 December	08:00 – 18:00	F	Piling installation
