COSTAIN SKANSKA Working on behalf of HS2

Atlas Road Preparation A&M Demolition

A&M/MotorSense Building






Scaffold Screens



Monitoring

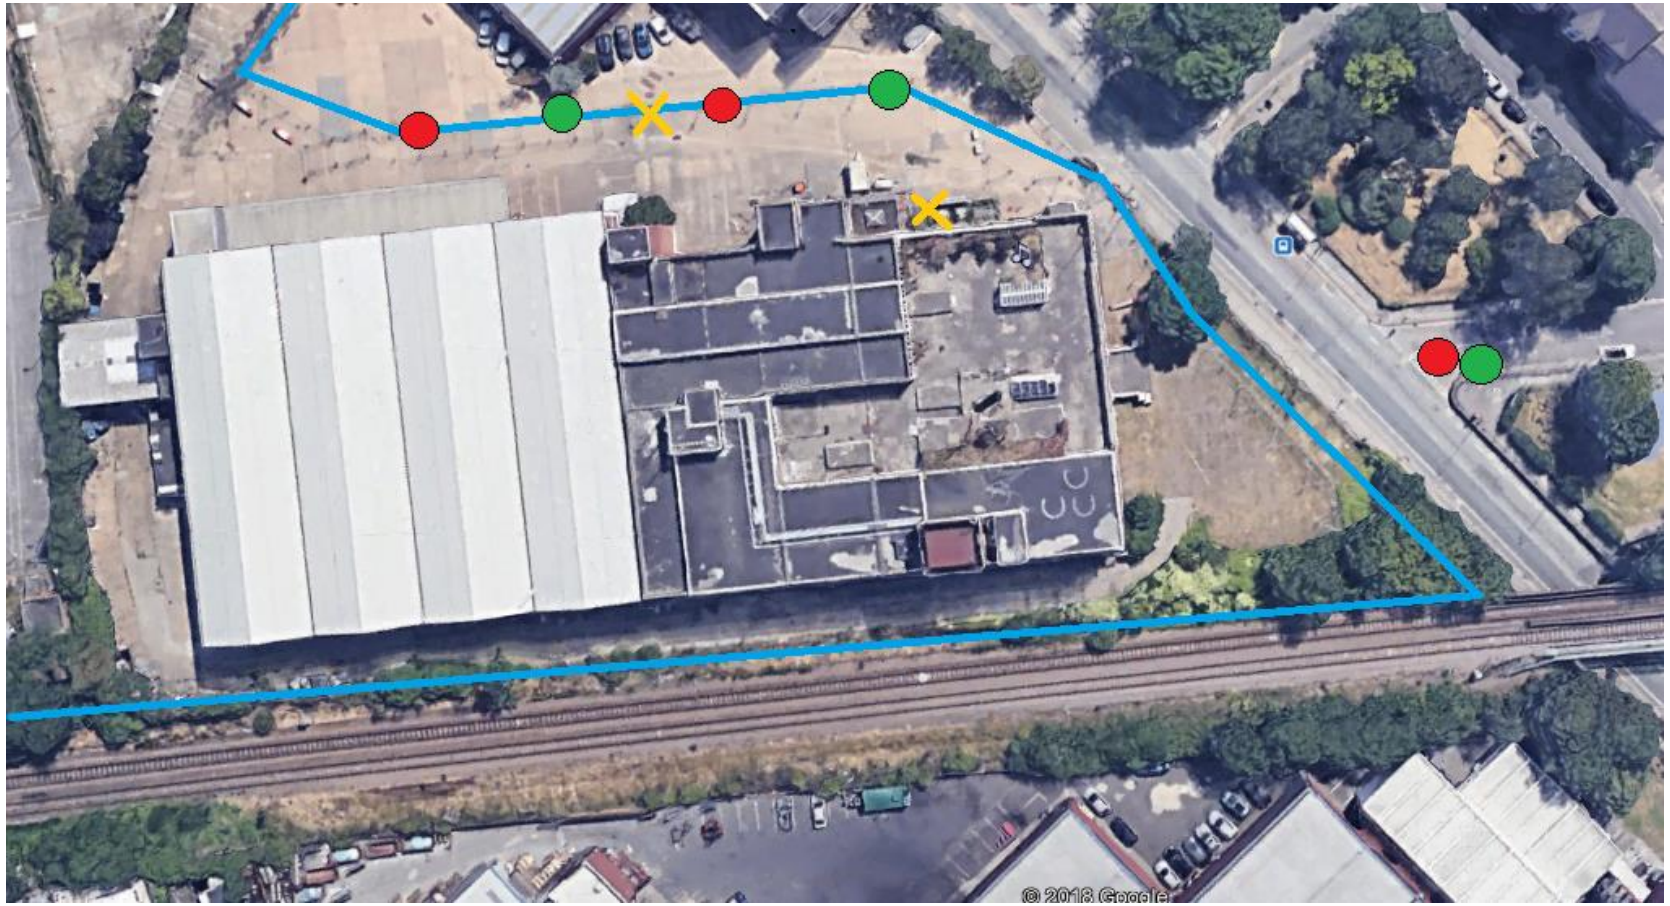

Noise Monitor

Dust Monitor

Vibration Monitor



Method of Demolition

- A long reach excavator, with muncher attachment, will be used to demolish the building.
- Low vibration and low noise methods to be implemented during demolition.
- The ground slab will remain, therefore no breaking of ground is required.
- Material will be processed away from Victoria Road side of site.

Dust Suppression





Dust suppression systems will be used throughout the demolition.
A fine mist will be constantly sprayed on the building to capture dust particles.

Programme

Scaffold Installation	– Complete 19/06/19
Demolition	– Start 24/06/19
Demolition	– Complete 31/07/19
Processing materials	– Complete 09/08/19

Start and completion dates subject to 3rd party approvals and any unforeseeable changes to the scope of works.
